
ID	Task Name	Duration	Predecessors
1	**WORK PROGRAMME FOR UPGRADE OF DATACENTRE INFRASTRUCTURE AT NIMC HQ, ABUJA**	**270 days**	
2	MOBILIZATION TO SITE	7 days	
3	ORDER AND DELIVERY OF DATA CENTRE EQUIPMEN	180 days	2
4	DEMOLITION AND ALTERATION	7 days	2
5	SUBSTRUCTURE WORK	21 days	4
6	CONCRETE FRAME AND BLOCK WORK	60 days	5
7	ROOFING	14 days	6
8	DOORS AND WINDOWS	10 days	7
9	CEILING FINISHES	10 days	8
10	WALL FINISHES	10 days	9
11	FLOOR FINISHES	10 days	10
12	MECHANICAL INSTALLATIONS	21 days	11
13	ELECTRICAL INSTALLATIONS	21 days	12
14	INSTALLATION OF DATA CENTRE EQUIPMENT	60 days	3
15	TESTING AND COMMISIONING	7 days	14
16	TRAINING AND CAPACITY BUILDING	15 days	15
17	HANDOVER	1 day	16

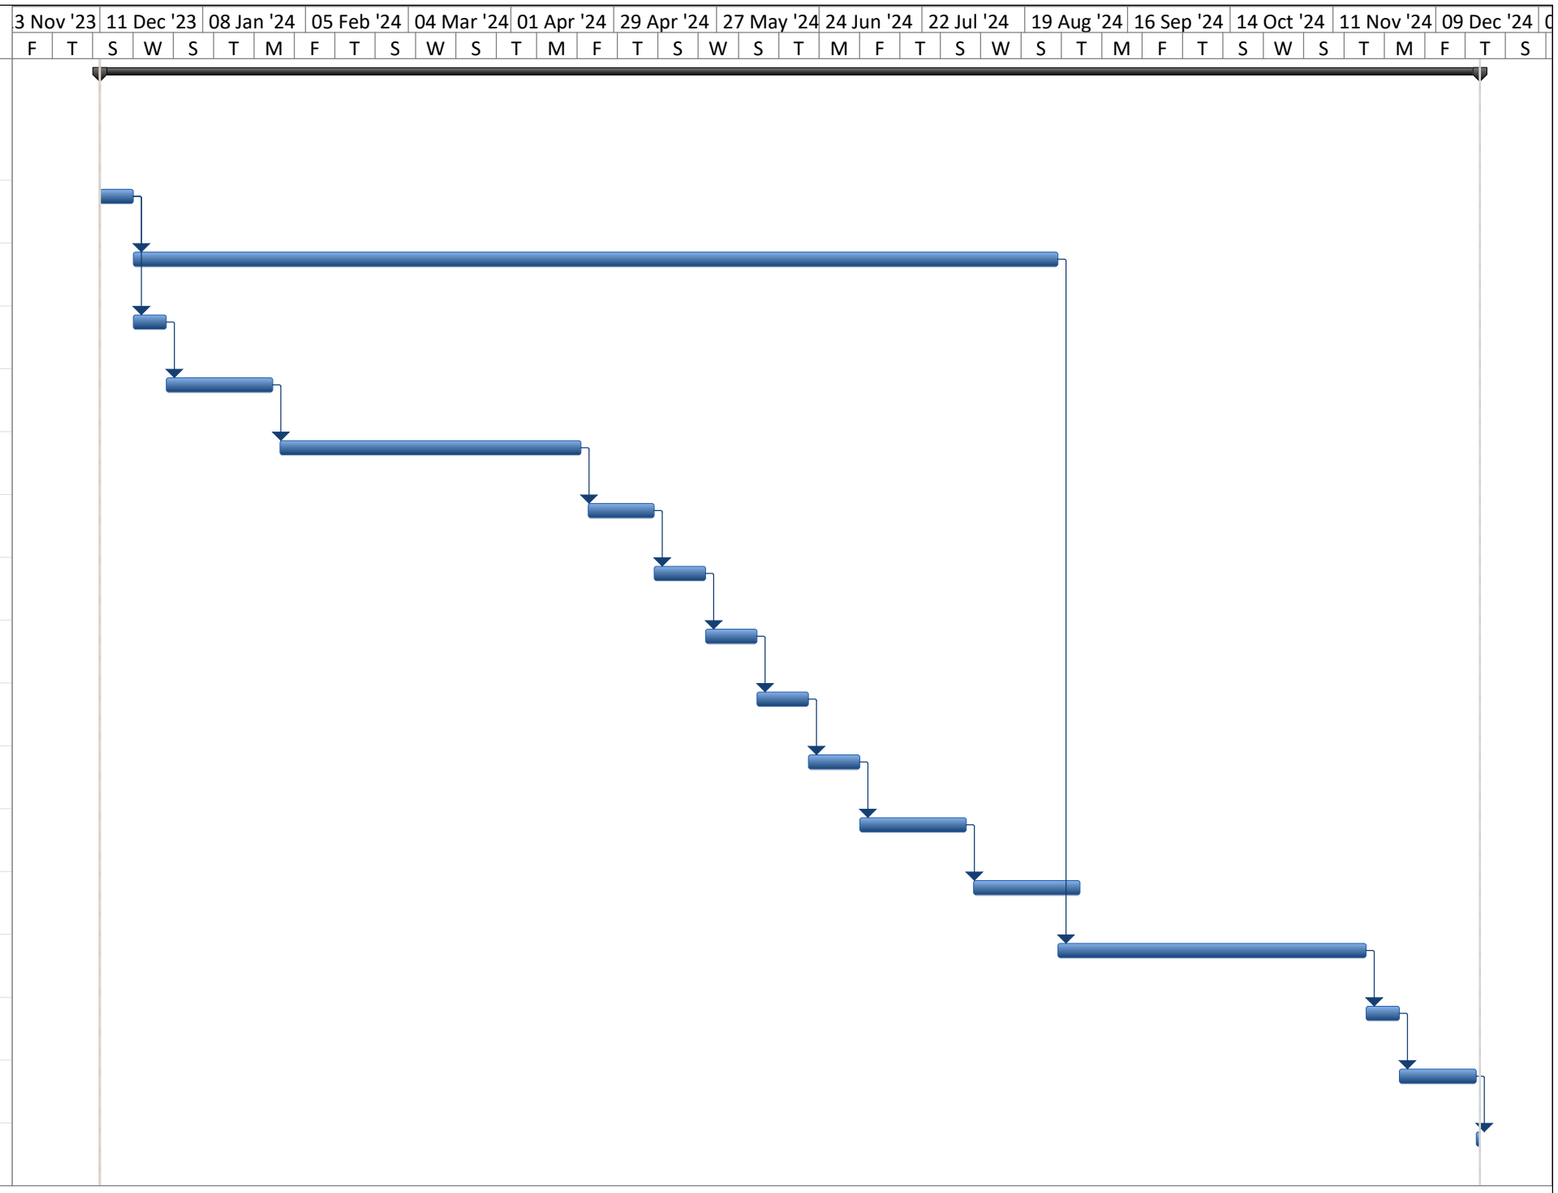

Project: ID4D Work Programme D
Date: Mon 11/12/23

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline	
Split	External Tasks	Inactive Summary	Manual Summary	Progress	
Milestone	External Milestone	Manual Task	Start-only		
Summary	Inactive Task	Duration-only	Finish-only		
